



## BUILDING DEPARTMENT ROBERT E. BYRNES, CONSTRUCTION OFFICIAL

## SIDEWALK, CURB & APRON CONSTRUCTION/REMOVAL PERMIT

JOI	BSITE LOCATION:	COMMINSTERIOR PLANTS AND		
Homeowner Name:		Teleph	Telephone #:	
		ractor Information		
Name:		Telephone #:		
Add	lress:			
Contractor License #: 13VH		Company Email:		
Nur	mber of slabs to be replaced:C	curb Amount in Feet:	Apron Size:	
Contact person responsible for jobsite:				
		RED INSPECTIONS:		
	CALL BEFORE YOU DIG WITH	HOUT MARKOUTS WO DEXCEPTIONS	RK CAN NOT BEGIN	
2. C	AFTER FORMS ARE LAID CONCRETE BEING POURED (TICKET COMPLETION OF WORK  CALL DPW AT: (201) 599-627	5 TO SCHEDULE REQUI		
	DO NOT WRIT	<u> FE BELOW THIS LINE</u>		
		APPROVED/DENIED	INSPECTOR & DATE	
1.	CORRECT FORM: (See the attached sidewalk form requirements)			
2.	BASE PREPARATION			
3.	EXPANSION JOINTS			
4.	BRUSHED FINISHED & EDGED			
5.	FORMS STRIPPED			
6.	RESTORATION	D UNDERSTOOD AND ACE	EES WITH THE	

BOROUGH OF RIVER EDGE ORDINANCE CHAPTER 362- STREETS & SIDEWALKS\*\*\*\*\*

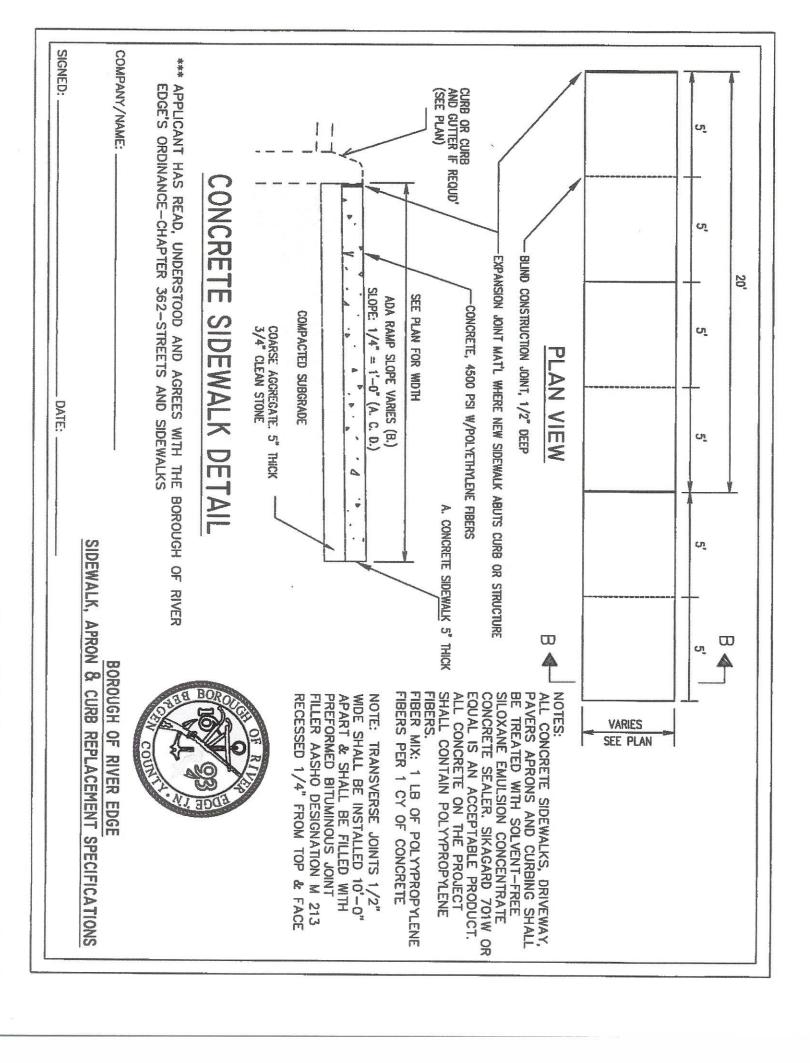

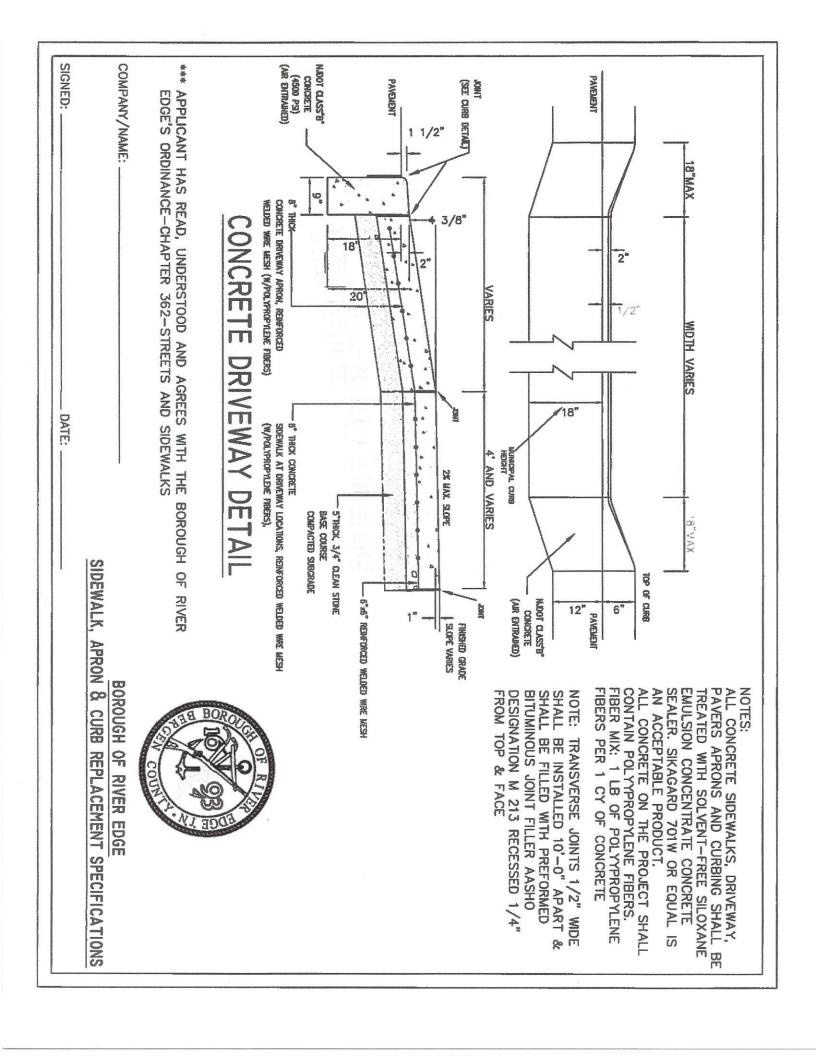

SIGNED: \*\*\* APPLICANT HAS READ, UNDERSTOOD AND AGREES WITH THE BOROUGH OF RIVER COMPANY/NAME: FINISHED GRADE EDGE'S ORDINANCE-CHAPTER 362-STREETS AND SIDEWALKS CLASS "B" 4500 PSI 18" /2" R 9"xI8" VERTICAL CURB DETAIL N 6" ರ್ Q DATE: 3/4" CLEAN STONE 2' MIN SAWCUT 1 1/4" R BASE COURSE

ALL CONCRETE ON THE PROJECT SHALL CONTAIN POLYYPROPYLENE FIBERS. FIBER MIX: 1 LB OF POLYYPROPYLENE FIBERS PER 1 CY OF CONCRETE NOTES:
ALL CONCRETE SIDEWALKS, DRIVEWAY, PAVERS APRONS AND CURBING SHALL BE TREATED WITH SOLVENT-FREE SILOXANE EMULSION CONCENTRATE CONCRETE SEALER, SIKAGARD 701W OR EQUAL IS AN ACCEPTABLE PRODUCT.

NOTE: TRANSVERSE JOINTS 1/2" WIDE SHALL INSTALLED 10'-0" APART & SHALL BE FILLED WITH PREFORMED BITUMINOUS JOINT FILLER AASHO DESIGNATION M 213 RECESSED 1/4" FROM TOP & FACE BE



BOROUGH OF RIVER EDGE

SIDEWALK, APRON & CURB REPLACEMENT SPECIFICATIONS
