



BUILDING DEPARTMENT
ROBERT E. BYRNES, CONSTRUCTION OFFICIAL

SIDEWALK, CURB & APRON CONSTRUCTION/REMOVAL PERMIT

JOB SITE LOCATION: _____

Homeowner Name: _____ Telephone #: _____

Contractor Information

Name: _____ Telephone #: _____

Address: _____

Contractor License #: **13VH** _____ Company Email: _____

Number of slabs to be replaced: _____ Estimated cost of work: _____

Contact person responsible for jobsite: _____ Contact #: _____

REQUIRED INSPECTIONS:

CALL BEFORE YOU DIG WITHOUT MARKOUTS WORK CAN NOT BEGIN

NO EXCEPTIONS


1. AFTER FORMS ARE LAID
2. CONCRETE BEING POURED (TICKET FROM CONCRETE TRUCK)
3. COMPLETION OF WORK

CALL DPW AT: (201) 599-6275 TO SCHEDULE REQUIRED INSPECTIONS

DO NOT WRITE BELOW THIS LINE

| | <u>APPROVED/DENIED</u> | <u>INSPECTOR & DATE</u> |
|---|------------------------|-----------------------------|
| 1. CORRECT FORM: (See the attached sidewalk form requirements) | _____ | _____ |
| 2. BASE PREPARATION | _____ | _____ |
| 3. EXPANSION JOINTS | _____ | _____ |
| 4. BRUSHED FINISHED & EDGED | _____ | _____ |
| 5. FORMS STRIPPED | _____ | _____ |
| 6. RESTORATION | _____ | _____ |

***** APPLICANT HAS READ, UNDERSTOOD AND AGREES WITH THE
BOROUGH OF RIVER EDGE ORDINANCE CHAPTER 362- STREETS & SIDEWALKS*****

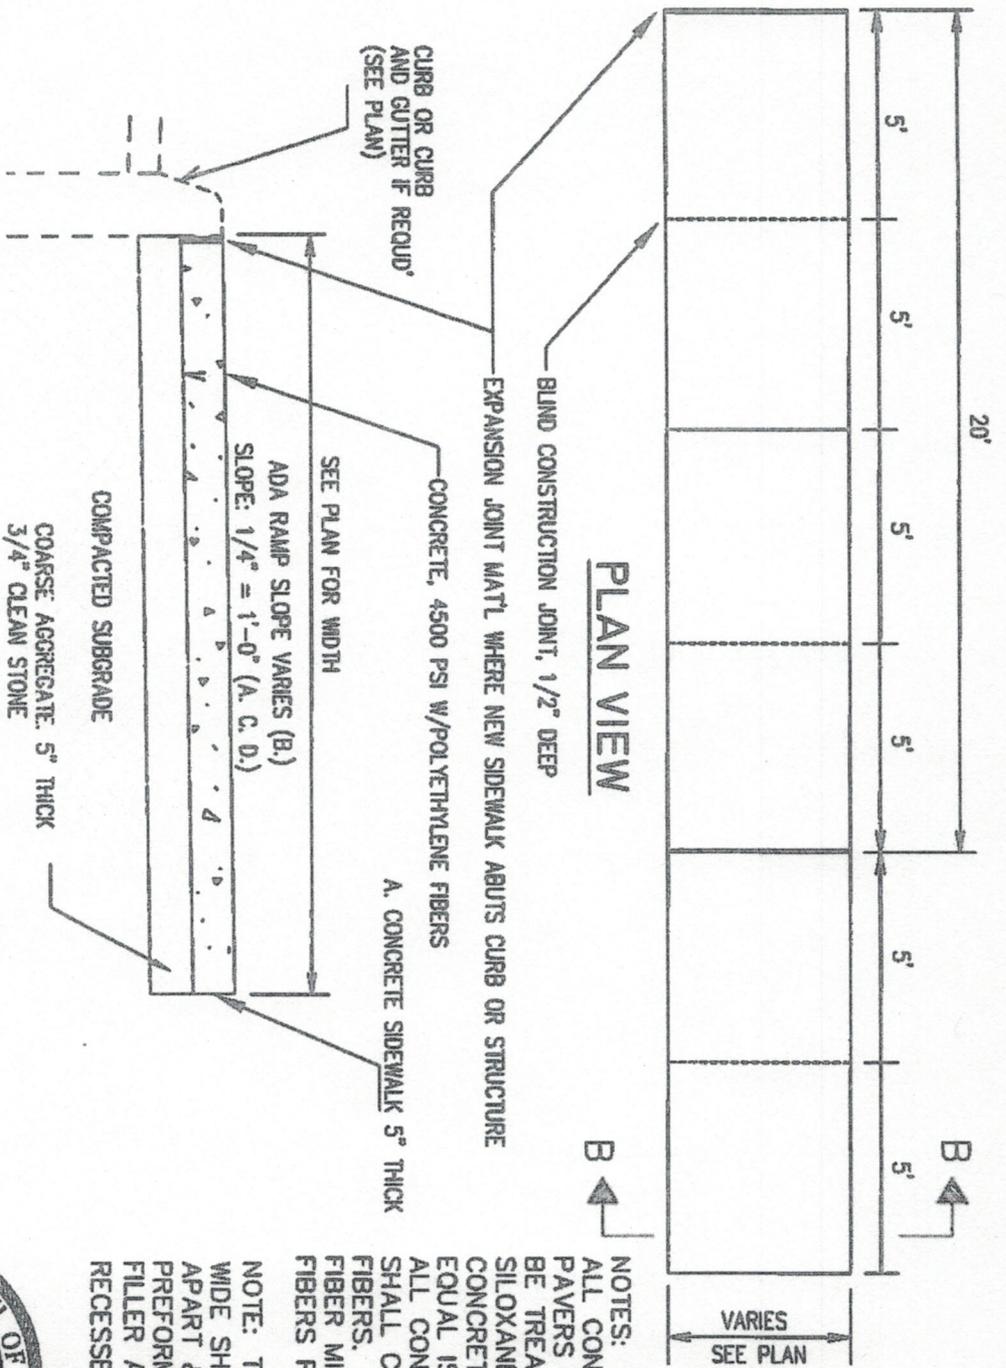

CONCRETE SIDEWALK DETAIL

*** APPLICANT HAS READ, UNDERSTOOD AND AGREES WITH THE BOROUGH OF RIVER EDGE'S ORDINANCE-CHAPTER 362-STREETS AND SIDEWALKS

COMPANY/NAME: _____

SIGNED: _____ DATE: _____

PLAN VIEW


B

VARIES
SEE PLAN


NOTES:

ALL CONCRETE SIDEWALKS, DRIVEWAY, PAVERS APRONS AND CURBING SHALL BE TREATED WITH SOLVENT-FREE SILOXANE EMULSION CONCENTRATE CONCRETE SEALER. SIKAGARD 701W OR EQUAL IS AN ACCEPTABLE PRODUCT. ALL CONCRETE ON THE PROJECT SHALL CONTAIN POLYPROPYLENE FIBERS.
 FIBER MIX: 1 LB OF POLYPROPYLENE FIBERS PER 1 CY OF CONCRETE

NOTE: TRANSVERSE JOINTS 1/2" WIDE SHALL BE INSTALLED 10'-0" APART & SHALL BE FILLED WITH PREFORMED BITUMINOUS JOINT FILLER AASHO DESIGNATION M 213 RECESSED 1/4" FROM TOP & FACE




BOROUGH OF RIVER EDGE
 SIDEWALK, APRON & CURB REPLACEMENT SPECIFICATIONS

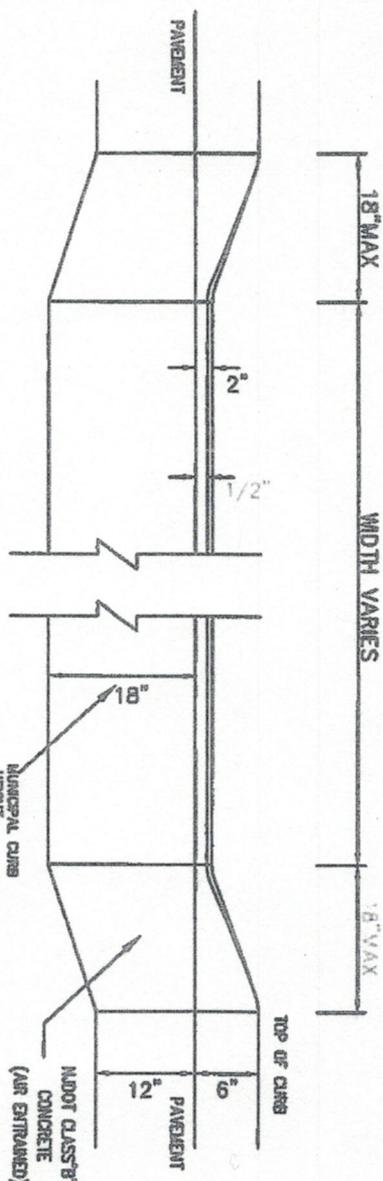

NOTES:
 ALL CONCRETE SIDEWALKS, DRIVEWAY, PAVERS APRONS AND CURBING SHALL BE TREATED WITH SOLVENT-FREE SILOXANE EMULSION CONCENTRATE CONCRETE SEALER. SIKAGARD 701W OR EQUAL IS AN ACCEPTABLE PRODUCT.
 ALL CONCRETE ON THE PROJECT SHALL CONTAIN POLYPROPYLENE FIBERS.
 FIBER MIX: 1 LB OF POLYPROPYLENE FIBERS PER 1 CY OF CONCRETE


NOTE: TRANSVERSE JOINTS 1/2" WIDE SHALL BE INSTALLED 10'-0" APART & SHALL BE FILLED WITH PERFORMED BITUMINOUS JOINT FILLER AASHO DESIGNATION M 213 RECESSED 1/4" FROM TOP & FACE

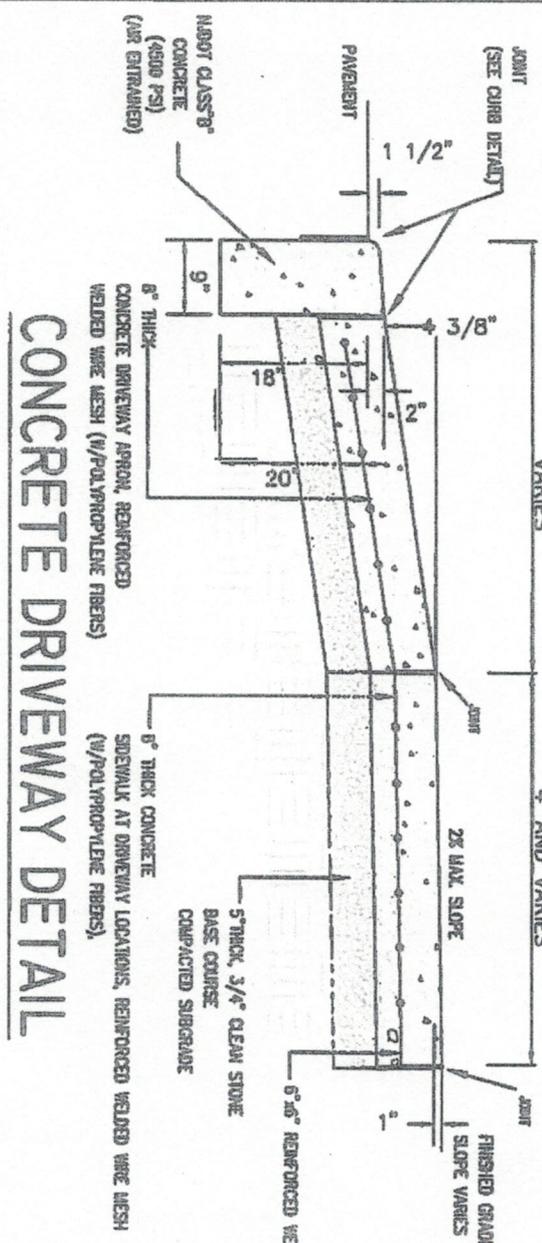

CONCRETE DRIVEWAY DETAIL


*** APPLICANT HAS READ, UNDERSTOOD AND AGREES WITH THE BOROUGH OF RIVER EDGE'S ORDINANCE-CHAPTER 362-STREETS AND SIDEWALKS

COMPANY/NAME: _____



**BOROUGH OF RIVER EDGE
 SIDEWALK, APRON & CURB REPLACEMENT SPECIFICATIONS**

SIGNED: _____ DATE: _____

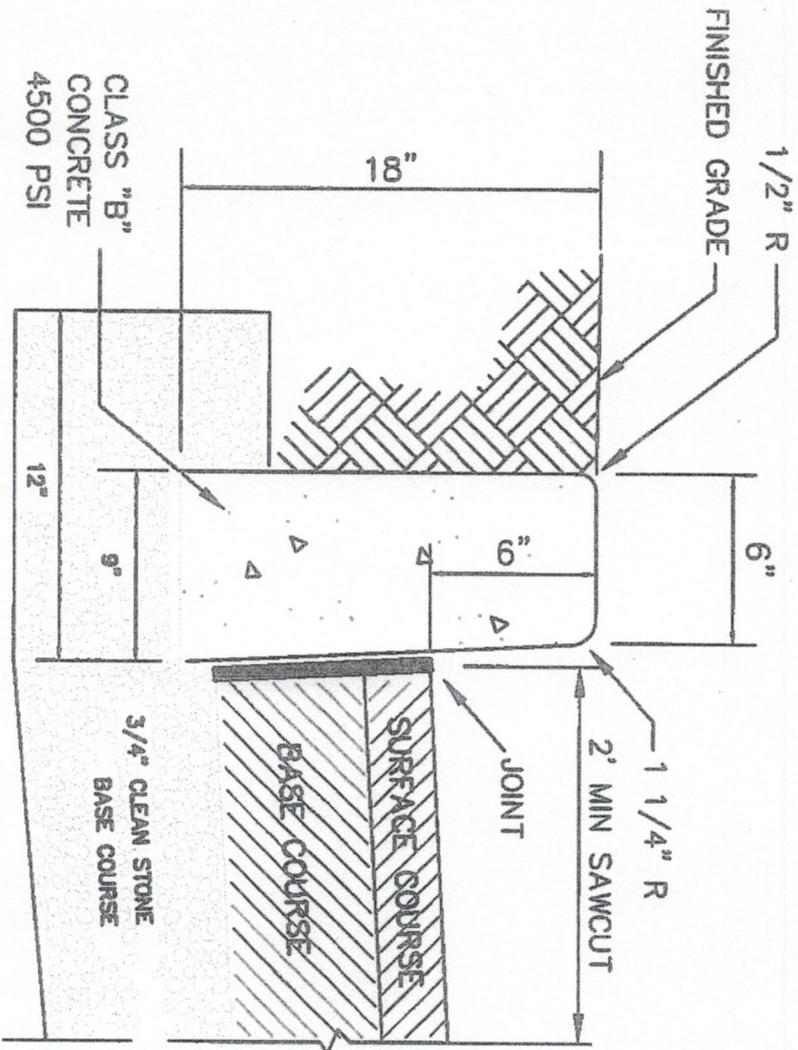

9"X18" VERTICAL CURB DETAIL

*** APPLICANT HAS READ, UNDERSTOOD AND AGREES WITH THE BOROUGH OF RIVER EDGE'S ORDINANCE-CHAPTER 362-STREETS AND SIDEWALKS

COMPANY/NAME: _____

SIGNED: _____ DATE: _____

NOTES:
 ALL CONCRETE SIDEWALKS, DRIVEWAY, PAVERS APRONS AND CURBING SHALL BE TREATED WITH SOLVENT-FREE SILOXANE EMULSION CONCENTRATE CONCRETE SEALER, SIKAGARD 701W OR EQUAL IS AN ACCEPTABLE PRODUCT. ALL CONCRETE ON THE PROJECT SHALL CONTAIN POLYPROPYLENE FIBERS. FIBER MIX: 1 LB OF POLYPROPYLENE FIBERS PER 1 CY OF CONCRETE

NOTE: TRANSVERSE JOINTS 1/2" WIDE SHALL BE INSTALLED 10'-0" APART & SHALL BE FILLED WITH PREFORMED BITUMINOUS JOINT FILLER AASHO DESIGNATION M 213 RECESSED 1/4" FROM TOP & FACE



BOROUGH OF RIVER EDGE
 SIDEWALK, APRON & CURB REPLACEMENT SPECIFICATIONS
